# Dashboard

▶ **Sections**

**SIREN Task 7.5 - Non-Technological Barriers to PM Circular Economy** · Phase 1 Active · Started 2026-03-13

**26% complete** - 38 tasks · 7 decisions (6 decided, 1 pending)

*Updated 2026-03-16 18:00 - may not reflect changes made outside `/work`*

---

# 🚨 Action Required

## Decisions

| Decision | Question | Doc |
|---|---|---|
| DEC-007 | Report structure and analytical framing (awaiting IVL template, task 7) | Pending |

*Open the doc, review options, check your selection, then run `/work`.*

## Review in progress

- ~~Task 2~~ - signed off (ude-instrument-design.md)
- ~~Task 3~~ - reviewed, placeholders filled except session dates (participant-invitation.md)
- ~~Task 4~~ - reviewed, placeholders filled except document date (consent-form.md)
- ~~Task 5~~ - reviewed, accepted with updates (PESTEL check, Claude workflow, omev.se, /search-log command) (literature-search-strategy.md)

## Still to review

| Task | What To Do | Where |
|---|---|---|
| 6 | Review facilitation guide (Session 1 + Session 2 protocols, between-session work, CLR reference, contingencies). Updated with breaks, Chat/Whiteboard, assistant role. | facilitation-guide.md |
| 30 | Review pre-workshop materials package (participant-facing: framing, IO Map, UDE explanation, scope guidance). Updated with Word template references. | pre-workshop-materials.md |
| 36 | Review anonymized participant profile template (6 columns, P1-P15 rows, stakeholder balance assessment) | participant-profiles-anon.md |
| 37 | Review data export workflow (M365 to repo pipeline, naming conventions, GDPR boundary, checklists). Updated with Word template + Chat references. | data-export-workflow.md |

## Your action needed (not document reviews)

| Task | What To Do |
|---|---|
| 7 | Provide IVL technical report template to `.claude/support/documents/`. Unblocks DEC-007 and Phase 5. |
| 8 | Recruit 8-10 workshop participants (over-recruit to 12-15). After invitation + consent form finalized. |
| 31 | Conduct internal trial run with IVL colleagues. After facilitation guide reviewed. |
| 39 | Test Teams Whiteboard with one external participant. Before trial run. May need IVL IT admin settings. |

## Placeholders to Fill Before Sending

These are scattered across deliverable documents. They can't be filled by Claude and risk being missed during proofreading.

**Participant invitation** (participant-invitation.md):

| Placeholder | What to fill | Status |
|---|---|---|
| `[response deadline]` | Deadline for confirming interest | |
| `[number] days` | How far in advance to share background materials (suggest 3-5) | |
| Session dates | Propose after initial responses | |

**Consent form** (consent-form.md):

| Placeholder | What to fill | Status |
|---|---|---|
| `[X] years` | Data retention period after project end | Ask IVL DPO |
| Recording policy | Will sessions be recorded? With separate consent? | Decision needed |
| `[DPO name or title]` | IVL's Data Protection Officer | Ask IVL |
| `[DPO email address]` | DPO contact email | Ask IVL |
| `[Address]` | IVL postal address for DPO section | Ask IVL |
| `[Date]` | Document date, set when finalised | |

*Contact info (email, phone) already filled in both documents.*

---

**Task 2 - Feedback:**
[Leave feedback here, then run /work complete 2]

**Task 3 - Feedback:**
[Leave feedback here, then run /work complete 3]

**Task 4 - Feedback:**
[Leave feedback here, then run /work complete 4]

**Task 5 - Feedback:**
[Leave feedback here, then run /work complete 5]

**Task 6 - Feedback:**
[Leave feedback here, then run /work complete 6]

**Task 7 - Feedback:**
[Leave feedback here, then run /work complete 7]

**Task 8 - Feedback:**
[Leave feedback here, then run /work complete 8]

**Task 30 - Feedback:**
[Leave feedback here, then run /work complete 30]

**Task 31 - Feedback:**
[Leave feedback here, then run /work complete 31]

**Task 36 - Feedback:**
[Leave feedback here, then run /work complete 36]

**Task 37 - Feedback:**
[Leave feedback here, then run /work complete 37]

---

# 📊 Progress

| Status | Count |
|---|---|
| Finished | 10 |
| Pending | 28 |

| Phase | Done | Total | Status |
|---|---|---|---|
| Phase 1 - Preparation & Planning | 10 | 13 | Active |
| Phase 2 - Workshop Execution | 0 | 6 | Blocked (Phase 1) |
| Phase 3 - Literature Review | 0 | 6 | Blocked (Phase 2) |
| Phase 4 - Analysis & Synthesis | 0 | 6 | Blocked (Phases 2, 3) |
| Phase 5 - Report Writing | 0 | 7 | Blocked (Phase 4, DEC-007) |

**Critical path:** ❗ Trial run → ❗ Session 1 → 👥 Between-session work → ... 9 more → Done *(12 steps)*

## Project Overview

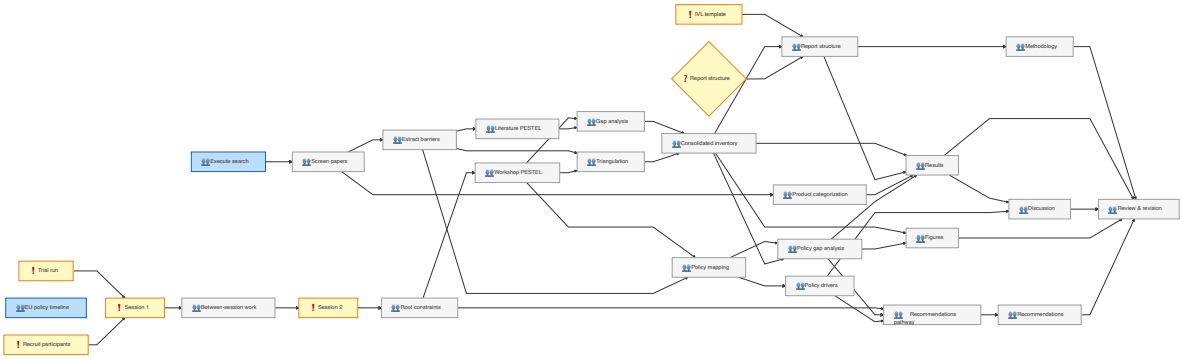


*Completed tasks (1, 2, 3, 4, 5, 6, 29, 30, 36, 37) removed from diagram - connections rerouted. Tasks 14 (execute search) and 38 (EU policy timeline) are active class: deps satisfied. Task 38 is standalone (no downstream deps).*

---

# 📋 Tasks

## Phase 1 - Preparation & Planning

| ID | Title | Status | Diff | Owner | Deps |
|---|---|---|---|---|---|
| 1 | Create IO Map (Goal, CSFs, NCs) for workshop validation | Finished | 5 | both | - |
| 2 | Prepare UDE collection instrument design | Finished | 4 | both | ~~DEC-002~~, ~~DEC-003~~, ~~DEC-005~~ |
| 3 | Draft participant invitation and information sheet | Finished | 3 | both | ~~1~~ |
| 4 | Prepare GDPR-compliant consent form | Finished | 3 | both | - |
| 5 | Define literature search strategy | Finished | 4 | both | ~~DEC-001~~, ~~DEC-006~~ |
| 6 | Prepare workshop facilitation guide | Finished | 6 | both | ~~1~~, ~~2~~, ~~DEC-002~~, ~~DEC-003~~, ~~DEC-005~~, ~~DEC-006~~ |
| 7 | Provide IVL technical report template | Pending | 1 | human | - |
| 29 | Prepare IO Map reference document | Finished | 4 | both | ~~1~~ |
| 30 | Prepare pre-workshop materials package | Finished | 3 | both | ~~1~~, ~~2~~, ~~29~~, ~~DEC-002~~, ~~DEC-003~~, ~~DEC-005~~ |
| 31 | Conduct internal trial run with IVL colleagues | Pending | 3 | human | ~~6~~ |
| 36 | Set up anonymized participant profile template | Finished | 2 | both | - |
| 37 | Define data export workflow for workshop outputs | Finished | 2 | both | ~~2~~ |
| 38 | Prepare EU policy timeline reference document | Pending | 4 | both | - |

*Phase 1: 10/13 complete (77%) - All implemented tasks finished. Remaining: task 7 (IVL template, human), task 31 (trial run, human), task 38 (EU policy timeline, both).*

## Phase 2 - Workshop Execution

| ID | Title | Status | Diff | Owner | Deps |
|---|---|---|---|---|---|
| 8 | Recruit 8-10 participants | Pending | 4 | human | ~~3~~, ~~4~~ |
| 9 | Execute Session 1 | Pending | 5 | human | ~~2~~, ~~6~~, 8, ~~30~~, 31 |
| 10 | Between-session work | Pending | 5 | both | 9 |
| 11 | Execute Session 2 | Pending | 5 | human | 10 |
| 12 | Document root constraints and injection points | Pending | 4 | both | 11 |
| 13 | PESTEL-classify workshop barriers (+ temporal tags) | Pending | 4 | both | 12, ~~DEC-004~~, ~~DEC-005~~, ~~DEC-006~~ |

*Phase 2: 0/6 complete - awaiting Phase 1 (tasks 8, 31; task 7 blocks Phase 5)*

## Phase 3 - Literature Review

| ID | Title | Status | Diff | Owner | Deps |
|---|---|---|---|---|---|
| 14 | Execute search strategy (WoS + grey literature) | Pending | 3 | both | ~~5~~, ~~DEC-006~~ |
| 15 | Screen and select papers | Pending | 4 | both | 14 |
| 16 | Extract barriers from literature | Pending | 4 | both | 15 |
| 17 | PESTEL-classify literature barriers (+ temporal tags) | Pending | 4 | both | 16, ~~DEC-004~~, ~~DEC-005~~, ~~DEC-006~~ |
| 18 | Map barriers to EU policy landscape | Pending | 5 | both | 13, 16, ~~DEC-006~~ |
| 32 | Develop product categorization table | Pending | 4 | both | 15 |

*Phase 3: 0/6 complete - awaiting Phase 2. Note: task 14 has all deps satisfied and could start early alongside workshop prep.*

## Phase 4 - Analysis & Synthesis

| ID | Title | Status | Diff | Owner | Deps |
|---|---|---|---|---|---|
| 19 | Gap analysis: workshop vs. literature (two-dimensional) | Pending | 5 | both | 13, 17, ~~DEC-004~~, ~~DEC-006~~ |
| 20 | Triangulation analysis | Pending | 4 | both | 13, 16 |
| 21 | Consolidated PESTEL barrier inventory | Pending | 4 | both | 19, 20 |
| 22 | Policy gap analysis | Pending | 4 | both | 18, 21 |
| 33 | Policy driver analysis | Pending | 3 | both | 18 |
| 34 | Recommendations pathway | Pending | 5 | both | 12, 22, 33 |

*Phase 4: 0/6 complete - awaiting Phases 2, 3*

## Phase 5 - Report Writing

| ID | Title | Status | Diff | Owner | Deps |
|---|---|---|---|---|---|
| 23 | Structure report per IVL template | Pending | 3 | both | 7, 21, DEC-007 |
| 24 | Write methodology section | Pending | 4 | both | 23, DEC-007 |
| 25 | Write results section | Pending | 5 | both | 21, 23, 32, 22, DEC-007 |
| 26 | Write discussion section | Pending | 4 | both | 25, 33, DEC-007 |
| 27 | Prepare figures | Pending | 4 | both | 21, 22, DEC-007 |
| 35 | Write recommendations section | Pending | 4 | both | 34 |
| 28 | Internal review and revision | Pending | 3 | both | 24, 25, 26, 27, 35, DEC-007 |

*Phase 5: 0/7 complete - awaiting Phase 4 and DEC-007*

*10/38 tasks complete (26%)*

---

# 📋 Decisions

| ID | Decision | Status | Selected |
|---|---|---|---|
| DEC-001 | Literature search databases | Decided | Option A - Web of Science |
| DEC-002 | UDE collection instrument | Decided | Option C - Combined (Forms + Teams) |
| DEC-003 | UDE collection timing | Decided | Option C - Pre-survey + live refinement |
| DEC-004 | PESTEL classification approach | Decided | Option C - Workshop-first with literature validation |
| DEC-005 | Technological scope boundary | Decided | Option A - Bright-line engineering exclusion |
| DEC-006 | Geopolitical dynamics and temporal validity | Decided | Option B - Temporal classification layer |
| DEC-007 | Report structure and analytical framing | Pending | Pending - awaiting task 7 |

---

# 💡 Notes

**Quick Links:**

- Spec v1 - project specification
- Vision document - methodology rationale and scoring
- Decisions - 7 decisions (6 decided, 1 pending)
- Project Management - staffing, budget, timeline
- Original LLM methodology: `/Users/erikemilsson/Developer/SIREN` (tag `v1.0-llm-methodology`)

**Key methodology decisions (this session):**

- DEC-004: Workshop PESTEL gaps + temporal gaps guide literature search emphasis (two-dimensional feedback loop)
- DEC-005: "Lab test" - engineering science is out of scope, technology systems are in scope
- DEC-006: Every barrier gets a temporal tag (Structural / Policy-driven / Emerging) alongside PESTEL category
- DEC-007: Report structure pending IVL template - may include causation framework section

# 👁️ Custom Views

## Task 7.5 Timeline

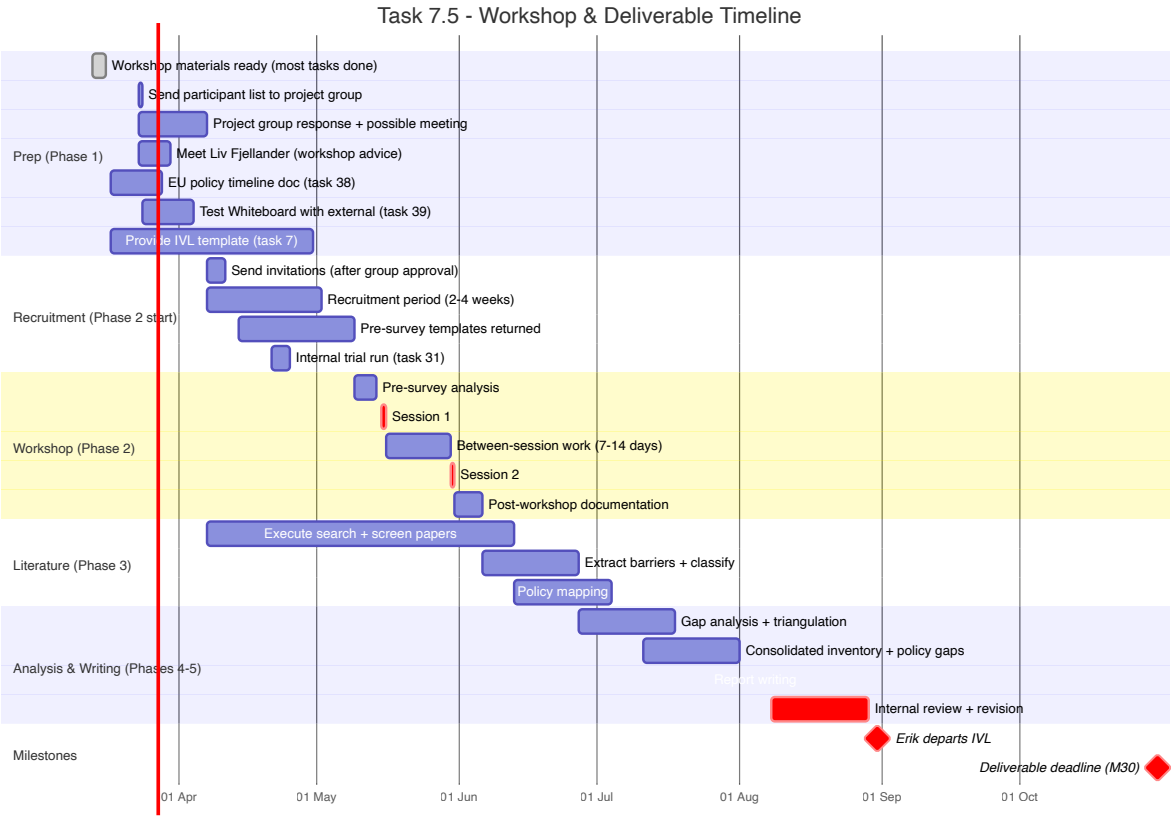


**Key dependencies:**

- Invitations go out after project group approves participant list (~April 7)
- Liv meeting needed before sessions, not before invitations
- Literature review (Phase 3) can run in parallel with recruitment and workshop
- Erik departs Aug 31; report should be in review by then (tighter than before)

*Dates are estimates based on: participant list sent March 23, 1-2 week project group response, 2-4 week recruitment, sessions in mid/late May. Writing and review compressed due to Aug 31 departure.*

---

*2026-03-16 18:00 UTC · 39 tasks · Spec aligned*
